




# Phase 2: Downtown Streetscape Project

April 26, 2024

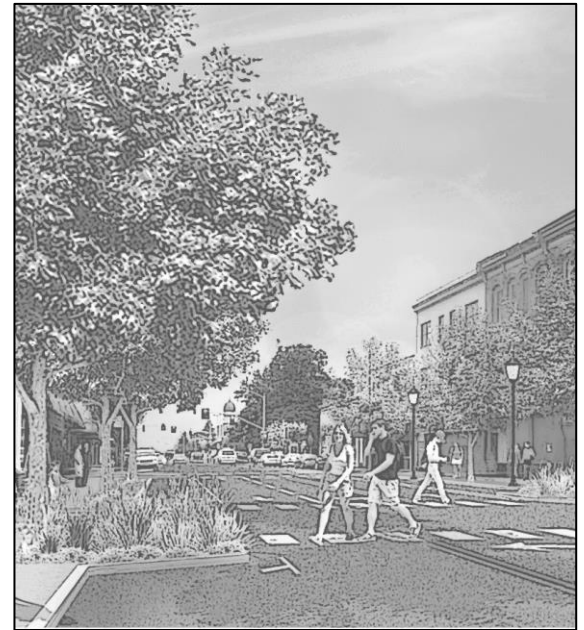

## Construction updates for the week of:

April 29<sup>th</sup> – May 3<sup>rd</sup>

**Important Update:** *The Urban Core Rehabilitation and Transportation Project, which will reconstruct Main, Perkins, and Gobbi Streets, is officially underway on Main Street. There will definitely be some overlap between this project and the completion of the streetscape project (anticipated in July), but we will do everything we can to mitigate impacts. We're working to maximize this construction season and improve as many streets as we can, so thank you in advance for your patience! Visit our webpage for more info and to sign up for email updates: [cityofukiah.com/ucrt](http://cityofukiah.com/ucrt)*

Back to streetscape...On the south side of the project, concrete crews are working the complete the formation of new curbs and gutters. Additionally, they are beginning to pour sidewalks on the west side, moving from the north to the south. Electric and landscaping crews will also be onsite working on electric infrastructure and irrigation lines for new landscaping. There will be temporary impacts to some driveways, but crews will provide advance notification and mitigate impacts to the best of our ability.

On the north side (Norton to Henry), installation of the brick band along the edge of the sidewalks will continue. All traffic signals in the construction area will remain on flash until the new pavement is in and the lane striping has occurred, likely late May/early June. **Important: the stop sign on State at Norton is being removed. Please use extra caution around these changed conditions, as it will take some time for people to adjust.**

**Where will the work occur?** Work on curbs, gutters, and sidewalks between Mill and Gobbi continues, along with electric infrastructure and irrigation; on the north side, installation of the brick band in the sidewalk.

**What are the construction days/hours?** Construction hours will be Monday-Friday, 7 a.m. - 6 p.m., depending on the weather.

**Will there be dust and noise?** Yes. There will be some noise associated with the south section; not much dust.

**Will there be any disruptions to parking access or streets?** Yes. On the south side, on-street parking in the construction zone will be closed; however, on-street parking on the north side of the project is open in most areas (see above). Pedestrian access to businesses will be maintained at all times. Through traffic on State Street will be allowed in both directions. Traffic signals at Gobbi/State and Mill/State and Scott/State will remain on flash.

Would you like to receive these updates by email? Call or send an email to Traci Boyl; contact info below.

### Streetscape Project Contact Information

Shannon Riley, Deputy City Manager: 707-467-5793 or [sriley@cityofukiah.com](mailto:sriley@cityofukiah.com)  
Traci Boyl, Senior Management Analyst: 707-467-5720 or [tboyl@cityofukiah.com](mailto:tboyl@cityofukiah.com)
